

Safety issues - Snowdon Towers shaft construction

First Step




Camera Position1370113.147ft, 258195.893ft, 779.640ft

Comment 1

StatusNew
UserHugo Martin
TextSignificant riser height (75cm > 25cm), also acting as an unprotected edge.
2026/1/05 14:28:33

Van Egress

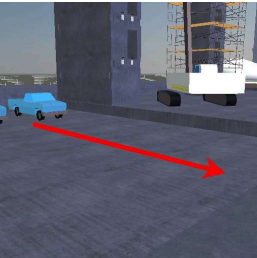

Camera Position1370078.631ft, 258168.164ft, 785.126ft

Comment 2

StatusNew
UserHugo Martin
TextPeople-plant interface between pedestrians and construction vehicles entering and leaving the site.
2026/1/05 14:29:40

Crane Slew




Camera Position1370110.262ft, 258185.827ft, 792.316ft

Comment 3

StatusNew
UserHugo Martin
TextPeople-plant interface between pedestrians and the crane, especially when slewing.
2026/1/05 14:32:04

Mixer Egress


Camera Position1370146.125ft, 258192.876ft, 800.890ft

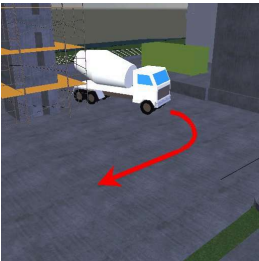

Comment 4

Status	New
User	Hugo Martin
Text	People-plant interface between pedestrians accessing the shaft and the mixer entering or leaving the site.
2026/1/05 14:32:52	

Second Step

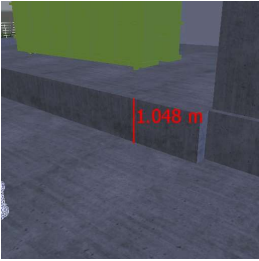

Camera Position 1370174.541ft, 258252.447ft, 786.646ft

Comment 5

Status	New
User	Hugo Martin
Text	Significant riser height (105cm > 25cm), also acting as an unprotected edge.
2026/1/05 14:33:25	
